Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float
1000	DEVELOP SCHEMATIC DESIGN AND	45	0	10APR09	19JUN09	
1010	REVIEW SCHEMATIC DESIGN AND PH	10	0	19JUN09	06JUL09	
1002	DEVELOP FINISH DESIGN AND	35	0	07JUL09	01SEP09	
1004	DEVELOP AND DELIVER FINAL	13	0	03SEP09	16SEP09	
1007	EXECUTE CONTRACT	3	0	23SEP09	25SEP09	
1008	SECURE FINANCING FOR PROJECT	10	0	28SEP09	14OCT09	
1005	AWARD DESIGN BUILD CONTRACT	0	0	09OCT09		
1006	PRECONSTRUCTION ACTIVITIES AND	5	0	12OCT09	14OCT09	
2092	OBTAIN P&Z APPROVAL	0	0	13OCT09		
2000	SITE CLEARING AND GRADING	5	0	19OCT09	29OCT09	
1009	CLOSE ON PROPERTY	3	0	20OCT09	20OCT09	
2002	BUILDING LAYOUT	2	0	26OCT09	27OCT09	
2004	FORM BUILDING SLAB	3	0	28OCT09	12NOV09	
1011	STORM DRAINAGE	5	0	02NOV09	03NOV09	
2006	ROUGH IN PLUMBING & BACKFILL	4	0	03NOV09	06NOV09	
2078	INSTALL UNDERGROUND DRAINAGE &	5	0	03NOV09	06NOV09	
2008	SLAB PREPARATION	3	0	09NOV09	12NOV09	
2010	POUR SLAB	2	0	13NOV09	13NOV09	
2012	WALL FRAMING	12	0	16NOV09	19NOV09	
2020	EXTERIOR WALL SHEATHING	2	0	23NOV09	08DEC09	
2014	ROOF FRAMING AND DECKING	10	0	24NOV09	04DEC09	
2090	INSTALL SITE UTILITIES	3	0	01DEC09	22DEC09	
2028	FLASH AND INSTALL WINDOWS	5	1	04DEC09	29DEC09	0
2016	ELECTRICAL ROUGH IN	10	0	10DEC09	23DEC09	
2022	RUN FASCIA BOARD	3	0	10DEC09	15DEC09	
2034	FRAME DRIVE THRU	4	0	10DEC09	15DEC09	
2032	DIG, PREP, & POUR ISO. FTGS FOR	1	0	11DEC09	11DEC09	
2018	PLUMBING ROUGH IN ABOVE SLAB	10	0	14DEC09	29DEC09	
2024	INSTALL ROOFING AND SHEET METAL	3	0	16DEC09	17DEC09	
2026	INSTALL DUCT WORK	15	6	21DEC09	06JAN10	56d
2030	LAY STONE WORK	20	3	21DEC09	04JAN10	38d
2062	SET HVAC EQUIP & INSTALL REF	2	1	22DEC09	29DEC09	4d
2042	INSTALL WOOD BLOCKING IN WALLS	2	2	29DEC09	30DEC09	3d
2074	SITE/PARKING LAYOUT	3	3	29DEC09	31DEC09	32d
2054	INSTALL WALL & CEILING INSULATION	4	4	30DEC09	05JAN10	0
2076	FORM & POUR CURB & GUTTER &	10	10	04JAN10	15JAN10	32d
2036	INSTALL EXT. SIDING & TRIM	10	10	05JAN10	18JAN10	38d
2044	HANG & FINISH DRY WALL	10	10	06JAN10	19JAN10	0
2080	FORM AND POUR EXT. SIDEWALKS	5	5	18JAN10	22JAN10	32d
2038	INSTALL EXT. SHINGLE SIDING	5	5	19JAN10	25JAN10	38d
2046	RUN INT TRIM & HANG DOORS	10	10	20JAN10	02FEB10	0
2082	ASPHALT PAVING	3	3	25JAN10	27JAN10	32d
2086	PARKING STRIPING & HDCP SIGNAGE	2	2	26JAN10	27JAN10	36d
2040	INSTALL SOFFIT, BRACKETS & MISC	5	5	26JAN10	01FEB10	38d
2084	FINE GRADING & GRASSING	4	4	28JAN10	02FEB10	32d
2048	PRIME AND 1ST COAT	4	4	03FEB10	08FEB10	0
2050	INSTALL CEILING GRID	4	4	09FEB10	12FEB10	0
2094	INSTALL CABINETWORK	10	10	15FEB10	26FEB10	0
2052	INSTALL LAY-IN LIGHT FIXTURES	5	5	15FEB10	19FEB10	2d
2056	INSTALL VCT FLOORING & BASE	5	5	15FEB10	19FEB10	19d
2060	HVAC DROPS & DIFFUSERS	3	3	15FEB10	17FEB10	26d
2064	INSTALL CEILING TILE	3	3	22FEB10	24FEB10	2d
2058	INSTALL & TRIMOUT PLUMBING	5	5	22FEB10	26FEB10	19d
2066	FINISH PAINTING	10	10	01MAR10	12MAR10	0
2068	INSTALL CARPET & BASE	4	4	15MAR10	18MAR10	0
2072	ELECTRICAL TRIMOUT	2	2	15MAR10	16MAR10	2d
2070	CLEAN & PUNCH	5	5	19MAR10	25MAR10	0
2088	OWNER MOVE IN	0	0		25MAR10	0

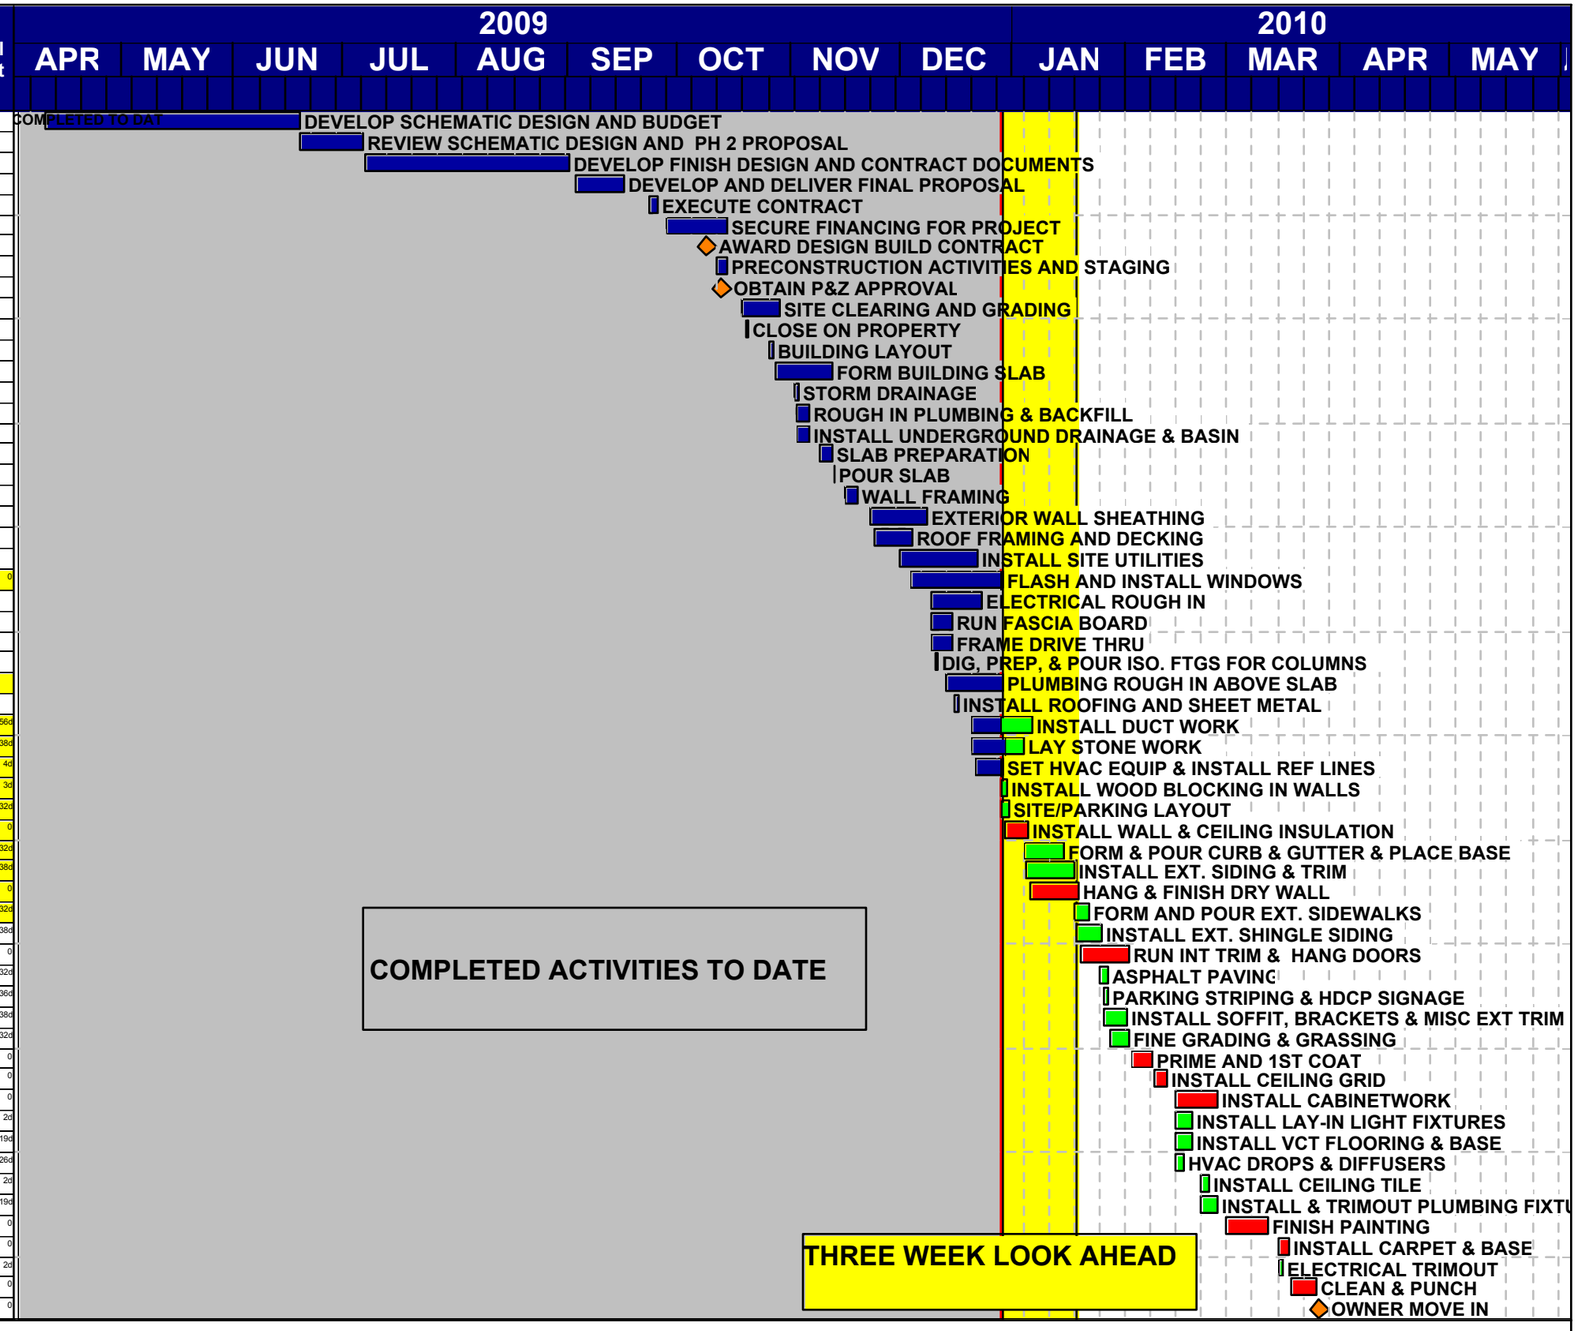

Start date	10APR09
Finish date	25MAR10
Data date	29DEC09
Run date	31DEC09
Page number	1A

© Primavera Systems, Inc.

Garbutt

DR. SOOS' PEDIATRICS OFFICE

Garbutt

Early bar
Progress bar
Critical bar
Summary bar
Start milestone point
Finish milestone poin
