Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish
1000	DEVELOP SCHEMATIC DESIGN AND	45	0	10APR09	19JUN09
1010	REVIEW SCHEMATIC DESIGN AND PH 2	10	0	19JUN09	06JUL09
1002	DEVELOP FINISH DESIGN AND	35	0	07JUL09	01SEP09
1004	DEVELOP AND DELIVER FINAL	13	0	03SEP09	16SEP09
1007	EXECUTE CONTRACT	3	0	23SEP09	25SEP09
1008	SECURE FINANCING FOR PROJECT	10	0	28SEP09	14OCT09
1005	AWARD DESIGN BUILD CONTRACT	0	0	09OCT09	
1006	PRECONSTRUCTION ACTIVITIES AND	5	0	12OCT09	14OCT09
2092	OBTAIN P&Z APPROVAL	0	0	13OCT09	
2000	SITE CLEARING AND GRADING	5	0	19OCT09	29OCT09
1009	CLOSE ON PROPERTY	3	0	20OCT09	20OCT09
2002	BUILDING LAYOUT	2	0	26OCT09	27OCT09
2004	FORM BUILDING SLAB	3	0	28OCT09	12NOV09
1011	STORM DRAINAGE	5	0	02NOV09	03NOV09
2006	ROUGH IN PLUMBING & BACKFILL	4	0	03NOV09	06NOV09
2078	INSTALL UNDERGROUND DRAINAGE &	5	0	03NOV09	06NOV09
2008	SLAB PREPARATION	3	0	09NOV09	12NOV09
2010	POUR SLAB	2	0	13NOV09	13NOV09
2012	WALL FRAMING	12	0	16NOV09	19NOV09
2020	EXTERIOR WALL SHEATHING	2	0	23NOV09	08DEC09
2014	ROOF FRAMING AND DECKING	10	0	24NOV09	04DEC09
2090	INSTALL SITE UTILITIES	3	0	01DEC09	22DEC09
2028	FLASH AND INSTALL WINDOWS	5	0	04DEC09	21JAN10 A
2016	ELECTRICAL ROUGH IN	10	0	10DEC09	23DEC09
2022	RUN FASCIA BOARD	3	0	10DEC09	15DEC09
2034	FRAME DRIVE THRU	4	0	10DEC09	15DEC09
2032	DIG. PREP. & POUR ISO. FTGS FOR	1	0	11DEC09	11DEC09
2018	PLUMBING ROUGH IN ABOVE SLAB	10	0	14DEC09	29DEC09
2024	INSTALL ROOFING AND SHEET METAL	3	0	16DEC09	17DEC09
2026	INSTALL DUCT WORK	15	0	21DEC09	20JAN10 A
2030	LAY STONE WORK	20	0	21DEC09	19JAN10 A
2062	SET HVAC EQUIP & INSTALL REF LINES	2	0	22DEC09	20JAN10 A
2042	INSTALL WOOD BLOCKING IN WALLS	2	0	29DEC09	30DEC09
2074	SITE/PARKING LAYOUT	3	0	29DEC09	31DEC09
2038	INSTALL EXT. SHINGLE SIDING	5	0	04JAN10	27JAN10 A
2076	FORM & POUR CURB & GUTTER &	10	0	04JAN10	14JAN10 A
2036	INSTALL EXT. SIDING & TRIM	10	0	05JAN10	20JAN10 A
2054	INSTALL WALL INSULATION	4	0	05JAN10	06JAN10 A
2040	INSTALL SOFFIT, BRACKETS & MISC	5	0	06JAN10	20JAN10 A
2044	HANG & FINISH DRY WALL	10	0	08JAN10	15JAN10 A
2096	EXTERIOR PAINTING	10	4	18JAN10	15FEB10
2048	PRIME AND 1ST COAT INTERIOR	12	0	20JAN10	27JAN10 A
2046	RUN INT TRIM & HANG DOORS	10	1	25JAN10	10FEB10
2050	INSTALL CEILING GRID	4	0	01FEB10	02FEB10
2060	HVAC DROPS & DIFFUSERS	3	0	01FEB10	10FEB10
2052	INSTALL LAY-IN LIGHT FIXTURES	5	0	09FEB10	09FEB10
2098	INSTALL IRRIGATION SYSTEM	5	5	10FEB10	16FEB10
2080	FORM AND POUR EXT. SIDEWALKS	5	5	10FEB10	16FEB10
2056	INSTALL VCT FLOORING & BASE	5	5	11FEB10	17FEB10
2066	FINISH PAINTING	10	10	11FEB10	10MAR10
2064	INSTALL CEILING TILE	3	3	11FEB10	15FEB10
2100	LANDSCAPING	10	10	17FEB10	02MAR10
2082	ASPHALT PAVING	3	3	17FEB10	19FEB10
2086	PARKING STRIPING & HDCP SIGNAGE	2	2	18FEB10	19FEB10
2058	INSTALL & TRIMOUT PLUMBING	5	5	18FEB10	24FEB10
2084	FINE GRADING & GRASSING	4	4	22FEB10	25FEB10
2094	INSTALL CABINETWORK	10	10	23FEB10	08MAR10
2068	INSTALL CARPET & BASE	4	4	11MAR10	16MAR10
2072	ELECTRICAL TRIMOUT	2	2	11MAR10	12MAR10
2070	CLEAN & PUNCH	5	5	17MAR10	23MAR10
2088	OWNER MOVE IN	0	0		23MAR10

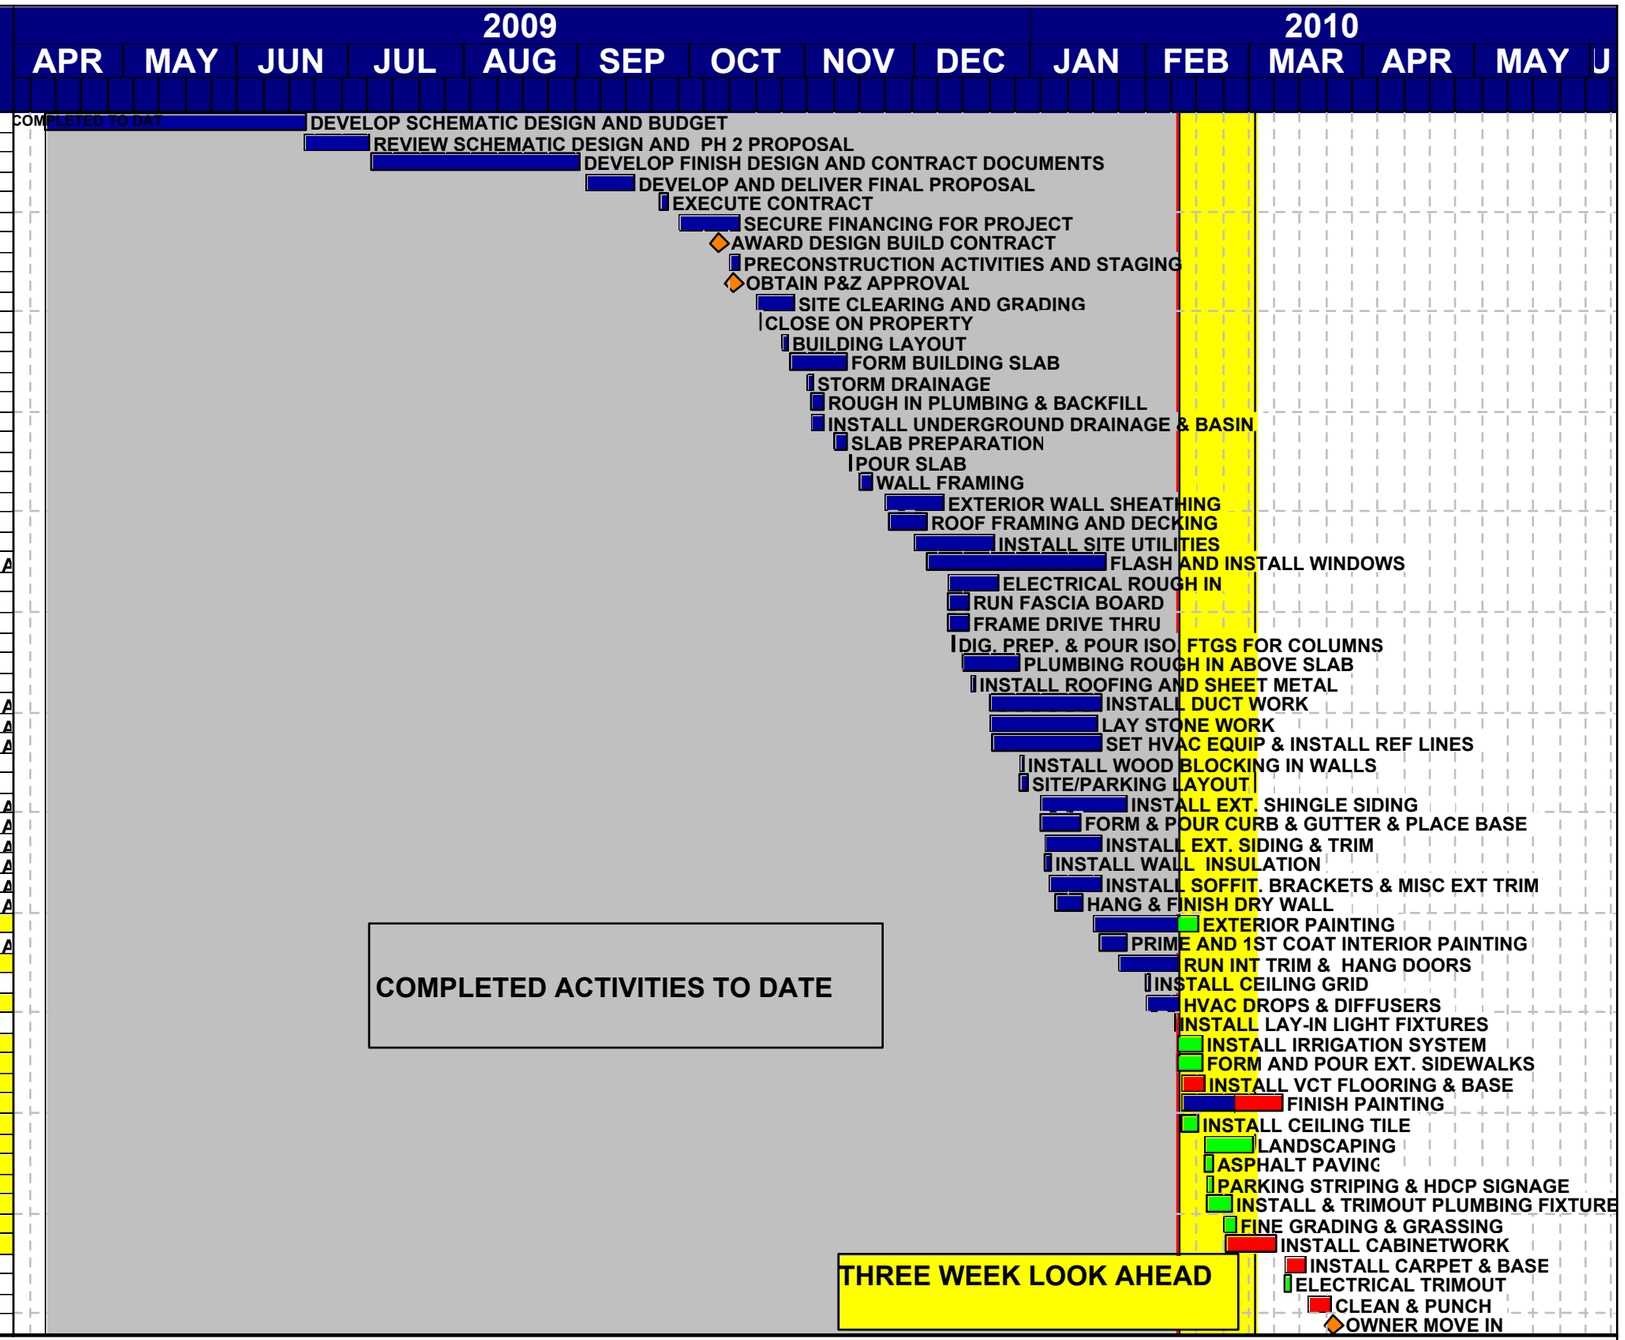

Start date	10APR09
Finish date	23MAR10
Data date	10FEB10
Run date	11FEB10
Page number	1A

© Primavera Systems, Inc.

Garbutt

DR. SOOS' PEDIATRICS OFFICE

Garbutt

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone poin
