Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish
GROUP #1(TRACY)					
1002	Stage demo	10d	5	11DEC08	16DEC08
1004	Balcony demo	15d	5	11DEC08	17DEC08
1008	Exterior demo	6d	5	16DEC08	05JAN09
1012	Initial Interior & ramp excavation	10d	5	16DEC08	22JAN09
1014	Underpining/Foundations	45d	5	20JAN09	25FEB09
1032	Remove steel beams at balcony	3d	5	05MAR09 A	09MAR09 A
1034	Structural steel @ 1st & 2nd Levels	40d	5	05MAR09 A	03JUN09
1024	Prep and Pour Basement slab	10d	5	20APR09 A	27MAY09 A
1030	Interior masonry / elevator shaft	20d	5	20APR09 A	18JUN09
1042	Prep & Pour Elevated slabs	7d	5	02JUN09 A	05JUN09
GROUP #2 (GEORGE					
1010	Retail area demo	10d	5	08DEC08 A	23DEC08
1016	Retail footings	15d	5	02JAN09 A	13JAN09
1022	Plbg underslab & service tie ins @ retail area	5d	5	15JAN09 A	21JAN09
1018	Retail masonry piers	5d	5	20JAN09 A	21JAN09
1020	Set retail steel col & channels	5d	5	31JAN09 A	03FEB09
1026	Demo retail load bearing walls	2d	5	03FEB09 A	05FEB09
1028	Retail floor framing & deck	10d	5	04FEB09 A	17FEB09
1036	Set remaining retail roof steel	5d	5	06APR09 A	10APR09
1038	Atrium roof framing and deck	5d	5	06APR09 A	09APR09
1044	Remaing atrium area demo & infill	15d	5	13APR09 A	30APR09
GENERAL TRADES					
1000	Mobilize	5d	5	01DEC08 A	12DEC08
1006	Existing sprinkler demo	10d	5	11DEC08 A	18DEC08
1100	Waterproofing and Backfill	15d	5	10FEB09 A	26FEB09
1102	Cut exterior Openings	11d	5	16MAR09 A	06JUL09
1050	Rough mechanical	30d	5	06APR09 A	20AUG09 A
1046	Metal stud framing	20d	5	11MAY09 A	17JUL09
1040	Roofing	30d	5	13MAY09 A	09NOV09 A
1104	Exterior Brick & Terra Cota Restoration	40d	5	13MAY09 A	16OCT09 A
1048	Rough plumbing	15d	5	18MAY09 A	30JUL09
1054	Rough electric	45d	5	01JUN09 A	27AUG09 A
1072	Set RTU's	2d	5	01JUN09 A	02JUN09
1052	Sprinkler rough in	30d	5	15JUN09 A	18AUG09 A
1056	Wood blocking	10d	5	26JUN09 A	16JUL09
1060	Insulation & drywall	20d	5	20JUL09 A	27AUG09 A
1106	Exterior Concrete Work	15d	5	30JUL09 A	04AUG09 A
1108	Aluminum Storefront	5d	5	05AUG09 A	11AUG09 A
1058	Office area plaster	10d	5	11AUG09 A	17SEP09
1062	Prime & 1st coat	10d	5	12AUG09 A	08SEP09
1064	Ceramic tile	15d	5	26AUG09 A	28AUG09 A
1076	Plumbing trim out	5d	5	31AUG09 A	03SEP09
1066	Acoustical grid	10d	5	01SEP09	10SEP09
1078	Cabinets and tops	3d	5	02SEP09	08SEP09
1070	HVAC trim out	15d	5	07SEP09	15DEC09
1080	Specialties	7d	5	07SEP09	10SEP09
1055	Install Elevator	25d	5	14SEP09	28OCT09 A
1068	Install Lighting	20d	5	14SEP09	17DEC09
1082	Doors & hardware	5d	5	08OCT09 A	15DEC09
1084	Finish paint	20d	34	12OCT09 A	31DEC09
1086	Floor Covering	10d	5	12OCT09 A	03DEC09
1116	Exterior Doors & Windows	2d	5	14OCT09 A	16DEC09
1074	Ceiling tiles	3d	5	26OCT09 A	08DEC09
1088	Electrical trim out	10d	5	26OCT09 A	16DEC09
1110	Marquis Restoration	15d	34	03NOV09 A	04JAN10
1112	Front Elevation & Soffit work	7d	5	11NOV09 A	18DEC09
1114	Aluminum Canopies	5d	5	16NOV09 A	18NOV09
1092	Test & balance	5d	5	14DEC09	17DEC09
1098	Install Freight Elevator	5d	50	14DEC09	09FEB10
1096	Install Theatrical Lighting System	15d	15d	27JAN10	17FEB10
1090	Final clean up	10d	5d	08FEB10	19FEB10
1212	ELEC WALL ROUGH-IN@ FOLLET BSMNT	4d	5	05OCT09 A	22OCT09 A
1214	O H ELEC R I @ FOLLET BSMNT	6d	5	05OCT09 A	19NOV09 A*
1204	METAL STUD WALLS @ FOLLET RETAIL	2d	5	12OCT09 A	15OCT09 A
1206	SOFFIT FRAMING @ FOLLET BASEMENT	2d	5	12OCT09 A	15OCT09 A
1208	SOFFIT FRAMING @ FOLLET RETAIL	10d	5	12OCT09 A	26NOV09 A
1216	ELEC WALL RI @ FOLLET RETAIL	6d	5	14OCT09 A	26OCT09 A
1202	DEMO FOLLET RETAIL AREA	2d	5	19OCT09 A	20OCT09 A
1218	O H ELEC R I @ FOLLET RETAIL	12d	5	19OCT09 A	26NOV09 A*
1232	INSTALL DUCTWORK IN FOLLET BSMNT	7d	5	19OCT09 A	26NOV09 A*
1228	PLUMBING @ JITTERY JOES	2d	5	20OCT09 A	16NOV09 A
1230	CUT HOLES FOR HVAC DUCTWORK @ BRICK WL	5d	5	20OCT09 A	22OCT09 A
1234	INSTALL DUCTWORK @ FOLLET RETAIL	10d	5	20OCT09 A	26OCT09 A
1236	HANG&FINISH S R @FOLLET BSMNT SOFFIT	5d	5	20OCT09 A	19NOV09 A*
1226	HANG&FINISH S R @ FOLLET RETAIL WALLS	5d	5	27OCT09 A	16NOV09 A
1220	INSTALL CAN LIGHTS @ FOLLET RETAIL	7d	5	02NOV09 A	26NOV09 A*
1242	INSTALL STOREFRONT @ FOLLET RETAIL	8d	5	03NOV09 A	23DEC09
1246	INSTALL WOOD TRIM @ FOLLET RETAIL	5d	5	16NOV09 A	19NOV09 A
1252	INSTALL DROPS & DIFFUSERS @ FOLLET AREAS	5d	5	16NOV09 A	19NOV09 A
1254	INSTALL LIGHTS @ FOLLET RETAIL	10d	5	16NOV09 A	19NOV09 A
1240	INSTALL SHUTTERS, DOORS & HRDWRE @ RET	3d	5	16NOV09 A	23NOV09 A*
1244	CEILING GRID @ FOLLET BSMNT & RETAIL	3d	5	16NOV09 A	20NOV09 A
1210	SPINKLER DROPS @ FOLLET RETAIL	3d	5	08DEC09	09DEC09
1238	PRIME S R @ ALL FOLLET AREAS	2d	5	08DEC09	09DEC09
1250	INSTALL MIRROR WALL TILE @ ENTRANCE	3d	5	08DEC09	16DEC09
1248	INSTALL MARQUIS SOFFIT	2d	5	14DEC09	16DEC09
1256	RESTORE TILE FLOOR @ MAIN ENTRANCE	3d	34	28DEC09	04JAN10
1260	CLEAN & PUNCH	5d	5d	04JAN10	11JAN10
2000	Submit on Concrete reinforcing	10d	5	03DEC08	23DEC08
2006	Submit on Concrete Mix Design	10d	5	23DEC08	30DEC08
2012	Submit on Structural Steel, Theatre Phase	15d	5	26DEC08	05JAN09
2008	Approve Concrete Mix Design	5d	5	31DEC08	13JAN09
2156	Submit on Structural Steel, Retail Phase	2d	5	01JAN09 A	21JAN09
2014	Approve Structural Steel, Theatre Phase	10d	5	02JAN09 A	09JAN09
1094	Submit on Concrete Reinforcing	10d	5	05JAN09 A	20JAN09
2016	Procure Structural Steel, Theatre phase	30d	5	09JAN09 A	20APR09
2010	Procure Ready Mix Concrete	1d	5	14JAN09 A	14JAN09
2158	Approve Structural Steel, Retail Phase	10d	5	21JAN09 A	28JAN09
2034	Procure Rough Carpentry Products	5d	5	26JAN09 A	27JAN09
2160	Procure Structural Steel, Retail Phase	15d	5	28JAN09 A	20APR09
2022	Approve Concrete Reinforcing	10d	5	02FEB09 A	13FEB09
2018	Submit on Metal Floor Decking	10d	5	02FEB09 A	05FEB09
2102	Submit on Elevator	20d	5	02FEB09 A	09FEB09
2132	Submit on HVAC Equipment & Materials	20d	5	05FEB09 A	06FEB09
2004	Procure Concrete Reinforcing	5d	5	09FEB09 A	10FEB09
2134	Approve HVAC Submittals	10d	5	09FEB09 A	20FEB09
2150	Submit on Electrical	15d	5	10FEB09 A	17FEB09
2042	Submit on Hollow Metal Doors & Frames	10d	5	16FEB09 A	20APR09
2144	Submit on Plumbing	10d	5	16FEB09 A	27FEB09
2104	Approve Elevator Submittals	10d	5	17FEB09 A	25FEB09
2136	Procure HVAC Equipment & Materials	40d	5	23FEB09 A	01JUN09
2152	Approve Electrical Submittals	5d	5	25FEB09 A	25MAR09 A
2046	Submit on Wood Doors	10d	5	02MAR09 A	12MAR09 A
2060	Submit on Finish Hardware	15d	5	02MAR09 A	13MAR09 A
2084	Submit on Acoustical Ceilings	10d	5	02MAR09 A	16MAR09 A
2120	Submit on Drywall	10d	5	02MAR09 A	16MAR09 A
2138	Submit on Fire Protection	20d	5	02MAR09 A	13MAR09 A
2086	Approve Acoustical Ceilings	10d	5	03MAR09 A	20MAR09 A
2122	Approve Drywall Materials	10d	5	03MAR09 A	20MAR09 A
2146	Approve Plumbing Submittals	10d	5	04MAR09 A	04MAY09 A
2126	Submit on Roofing Materials	10d	5	12MAR09 A	16APR09
2070	Procure Restore Wood Windows	30d	5	16MAR09 A	02SEP09
2140	Approve Fire Protection Submittals	10d	5	16MAR09 A	30APR09
2022	Procure Metal Floor Decking	15d	5	06APR09 A	20APR09
2108	Submit on Masonry	10d	5	06APR09 A	13APR09
2128	Approve Roofing Submittals	10d	5	15APR09 A	04MAY09 A*
2044	Approve Hollow Metal Doors & Frames	5d	5	20APR09 A	24APR09
2046	Procure Hollow Metal Doors & Frames	15d	5	27APR09 A	04AUG09 A
2054	Submit on Aluminum Storefront	10d	5	30APR09 A	04MAY09 A
2028	Procure Miscellaneous Metals	15d	5	04MAY09 A	18MAY09 A
2062	Approve Finish Hardware	10d	5	04MAY09 A	18MAY09 A
2110	Approve Masonry	10d	5	04MAY09 A	15JUN09
2130	Procure Roofing Materials	2d	5	04MAY09 A	06MAY09 A
2050	Approve Wood Doors	10d	5	13MAY09 A	20MAY09 A
2096	Submit on Accessories & Specialties	15d	5	18MAY09 A	24JUN09
2020	Approve Metal Floor Decking	10d	5	20MAY09 A	01JUN09
2056	Approve Aluminum Storefront	10d	5	01JUN09 A	15JUN09
2124	Procure Drywall Materials	10d	5	01JUN09 A	01SEP09
2106	Procure Elevator	25d	5	17JUN09 A	28JUL09
2154	Procure Electrical Submittals	10d	5	17JUN09 A	30JUN09
2112	Procure Masonry Products	5d	5	25JUN09 A	29JUL09
2142	Procure Fire Protection Materials	20d	5	01JUL09 A	21JUL09
2098	Approve Accessories & Specialties	10d	5	06JUL09 A	20JUL09
2052	Procure Wood Doors	20d	5	22JUL09 A	28OCT09
2078	Submit on Tile & Marble	15d	5	22JUL09 A	30JUL09
2080	Approve Tile & Marble	10d	5	29JUL09 A	03AUG09 A
2058	Procure Aluminum Storefront	15d	5	30JUL09 A	10AUG09 A
2148	Procure Plumbing Materials	15d	5	03AUG09 A	27AUG09 A
2088	Procure Acoustical Ceilings	10d	5	17AUG09 A	21AUG09 A
2076	Procure Stucco & Plaster	1d	5	24AUG09 A	25AUG09 A
2026	Approve Miscellaneous Metals	10d	5	25AUG09 A	01SEP09
2064	Procure Finish Hardware	20d	5	25AUG09 A	27NOV09 A
2090	Submit on Floor Covering	15d	5	25AUG09 A	01SEP09
2082	Procure Tile & Marble	15d	5	26AUG09 A	26AUG09 A*
2094	Procure Floor Covering	20d	5	02SEP09 A	12OCT09 A
2100	Procure Accessories & Specialties	15d	5	02SEP09 A	22SEP09
2116	Procure Freight Elevator	22d	22d	03NOV09 A	01FEB10
2118	Approval of Theatrical Package by College	1d	5d	07DEC09	08JAN10
2114	Procure Theatrical Lighting System	15d	15d	08JAN10	27JAN10

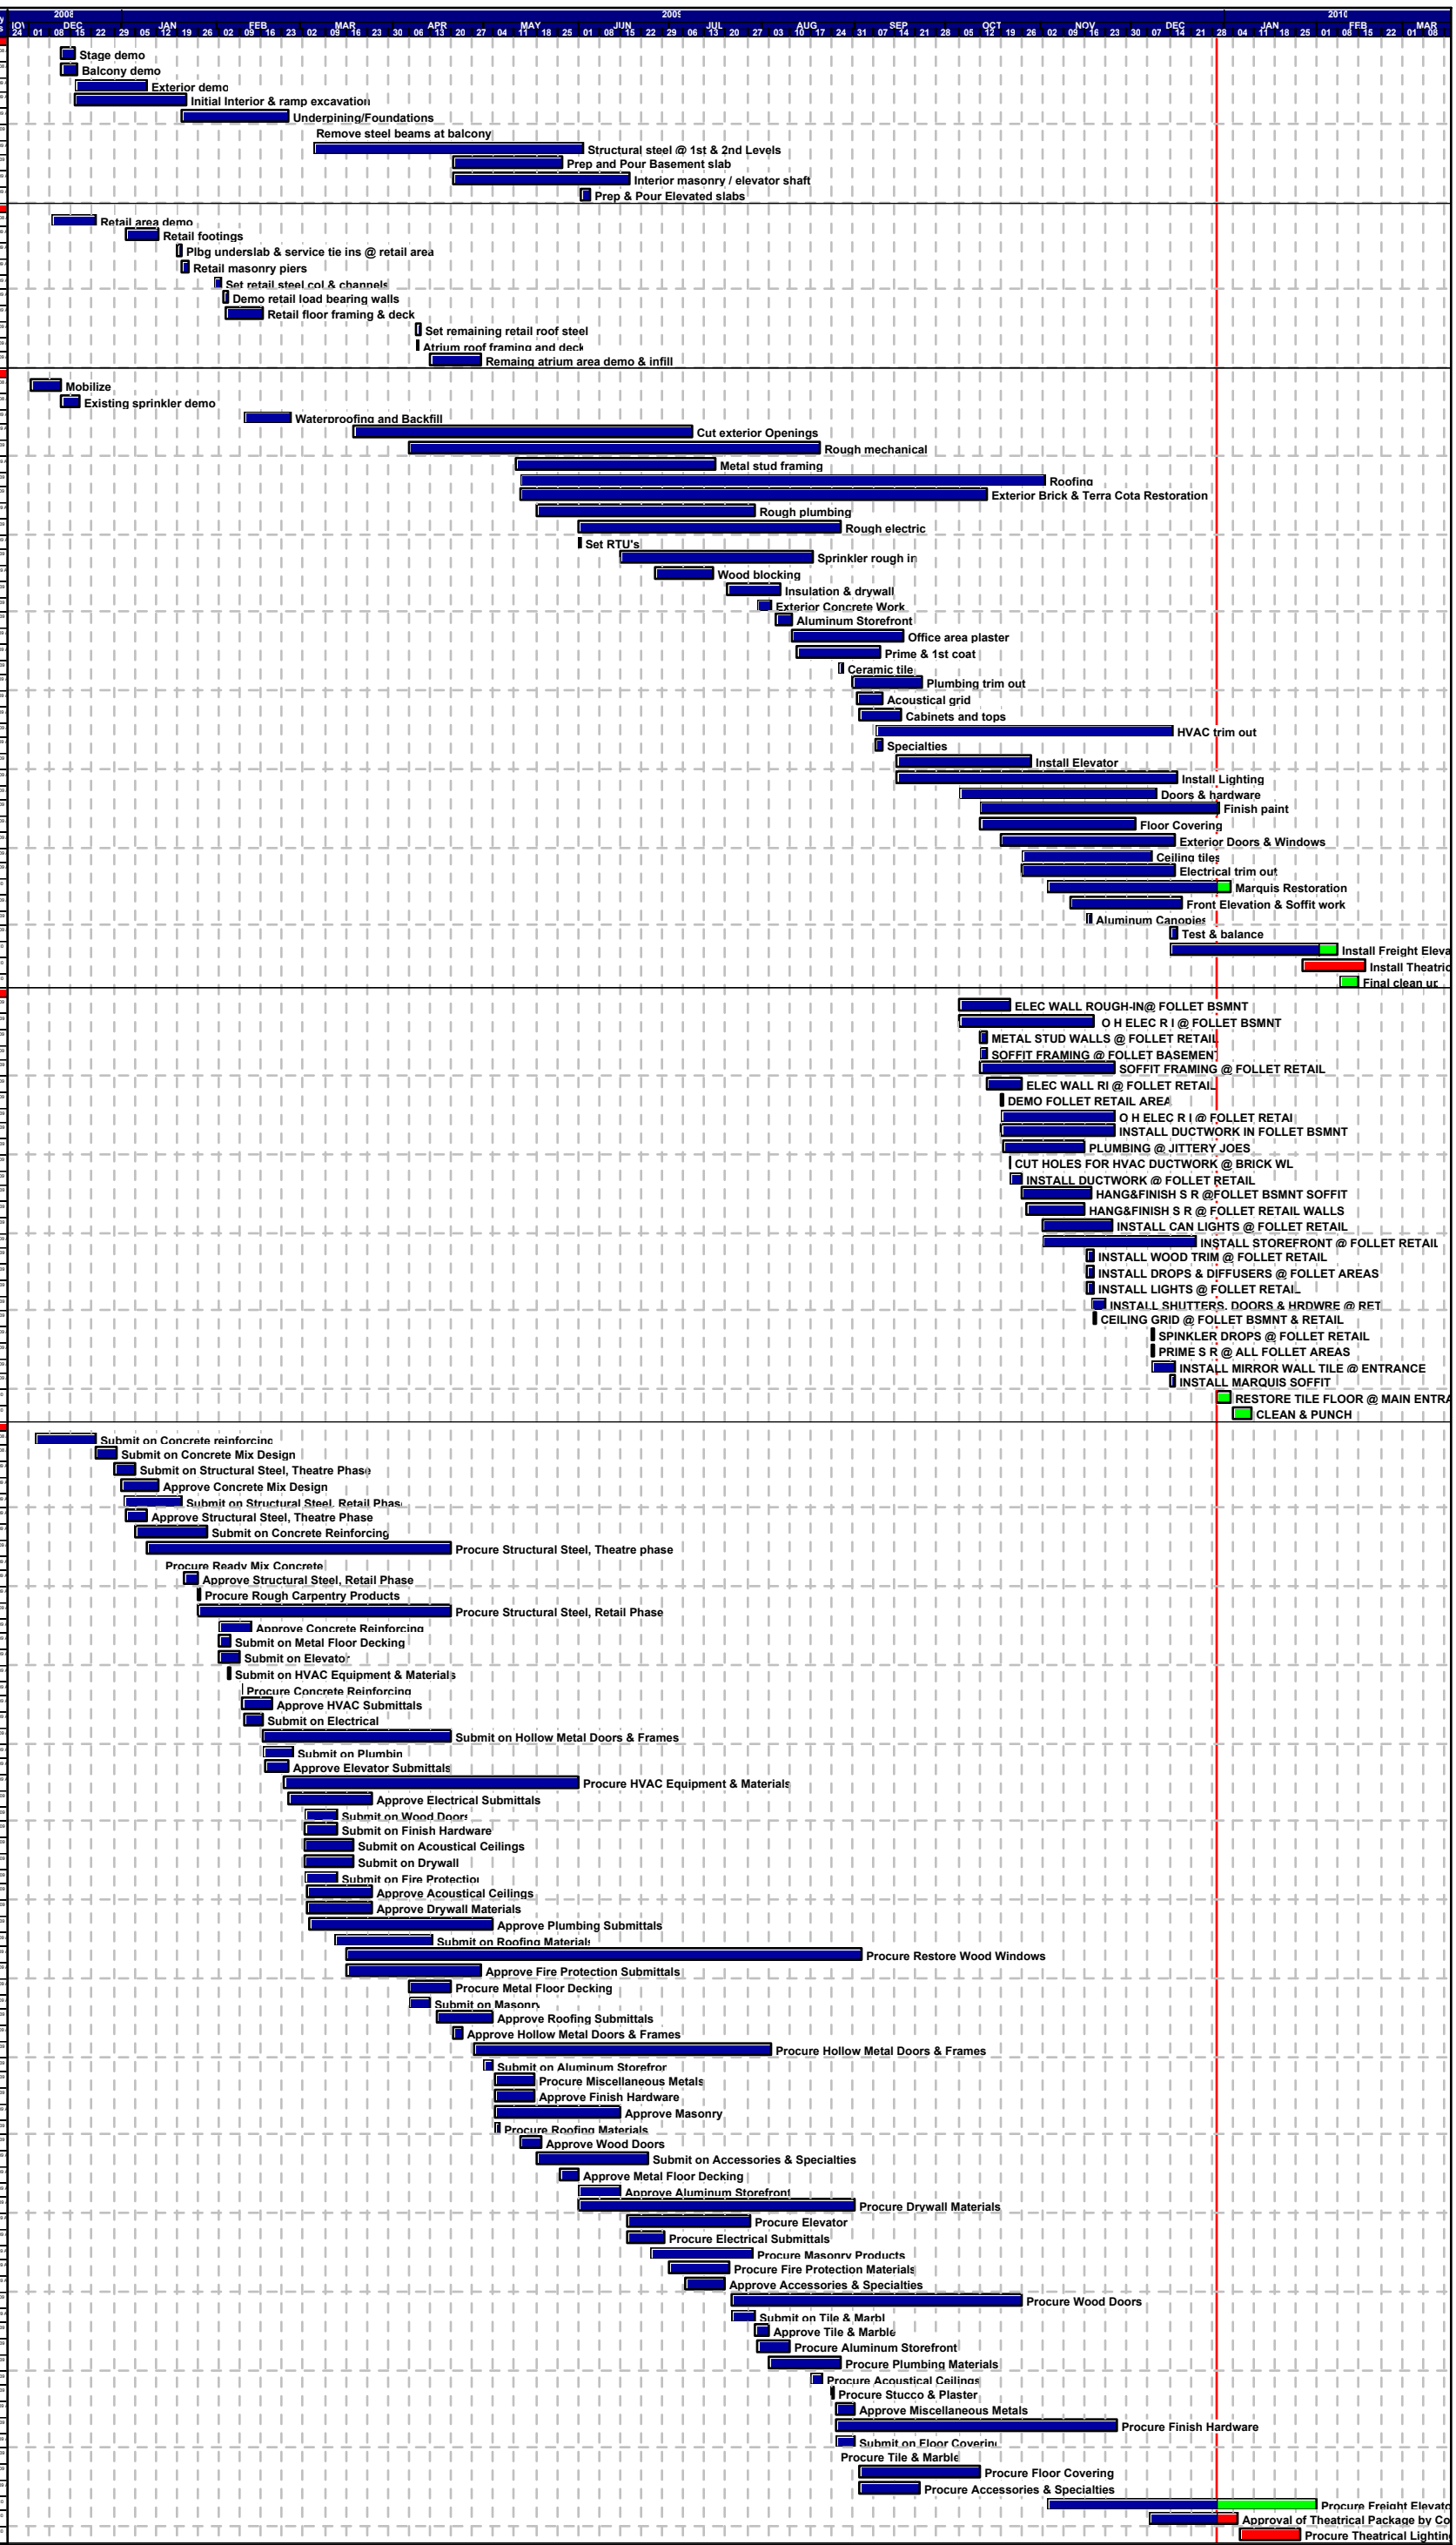

Start date	01DEC08
Finish date	17FEB10
Data date	20JAN09
Run date	26JAN09
Page number	1A

© Primavera Systems, Inc.

Garbutt-Christman, LLC
BOOKSTORE & BLACK BOX THEATREGarbutt-Christman, LLC

Early bar
Progress bar
Critical bar
Summary bar
Start milestone
