Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	%
Intermediate Construction Package							
1084	Remove Decking & Handrail @Breezway	5	0	01SEP09 A	18SEP09 A		100
1094	Remove Porch Ceiling	5	0	01SEP09 A	18SEP09 A		100
1074	Sprinkler Rough-In Attic	6	0	28SEP09 A	07OCT09 A		100
1090	1st Level Eave Soffit	15	0	01OCT09 A	19OCT09 A		100
1100	Remove Damaged Porch Columns	4	0	01OCT09 A	08OCT09 A		100
1020	Window Reinstalation	5	0	05OCT09 A	19MAY10 A		100
1072	Remove & Tag Light & Plumbing Fixtures	5	0	07OCT09 A	22OCT09 A		100
1000	Porch Rough-In Sprinkler	5	0	08OCT09 A	14OCT09 A		100
1102	Resolve Structural @ Porches	5	0	09OCT09 A	28OCT09 A		100
1050	Sprinkler Verticals	5	0	14OCT09 A	20OCT09 A		100
1004	Rough - In Electrical at Porch	3	0	19OCT09 A	21OCT09 A		100
1054	2nd Floor Sprinkler RI	10	0	21OCT09 A	04NOV09 A		100
1056	1st Floor Sprinkler RI	15	0	22OCT09 A	27OCT09 A		100
1032	Underground Electrical	15	0	26OCT09 A	27OCT09 A		100
1066	Electrical Rough-In @ Attic & Cupola	13	0	26OCT09 A	02DEC09 A		100
1068	Electrical RI 2nd Floor	20	0	26OCT09 A	04DEC09 A		100
1006	Resolve Structural Issues @ cupola	5	0	27OCT09 A	02NOV09 A		100
1092	2nd Level Eave Soffit	10	0	27OCT09 A	09NOV09 A		100
1008	Procure Structural Members	10	0	18NOV09 A	18NOV09 A		100
1070	Electrical RI 1st Floor	30	0	18NOV09 A	24NOV09 A		100
1104	Repair Foundation Structural Repair @ Main	20	0	18NOV09 A	21JAN10 A		100
1108	Floor Decking @ Porch	5	0	01DEC09 A	19FEB10 A		100
1118	Analyze finish samples of fixtures by Crenshaw	10	0	16DEC09 A	19JAN10 A		100
1058	Electrical Rough-In Crawlspace	10	0	21DEC09 A	19JAN10 A		100
1086	Procure Corbells	10	0	21DEC09 A	11JAN10 A		100
1116	Sprinkler drops at porch	1	0	21DEC09 A	22DEC09 A		100
1088	Repair and iNSTALL Corbell Brackets	5	0	12JAN10 A	22JAN10 A		100
1098	Reinstall Porch Ceiling	10	0	19JAN10 A	17FEB10 A		100
1120	CLEAN, CONSERVE AND REPAIR	40	0	19JAN10 A	13MAY10 A		100
1018	Electrical Service to WheelChair Lift	4	0	22JAN10 A	25MAR10 A		100
1014	Concrete Foundation @ Wheelchair Lift	5	0	25JAN10 A	11MAR10 A		100
1024	Mock-up of light fixtures	25	0	03FEB10 A	08MAR10 A		100
1030	Septic tank Installation	3	0	03FEB10 A	05FEB10 A		100
1038	Concrete Pad & Foundations Under house	7	0	03FEB10 A	11FEB10 A		100
1110	Reinstall Porch Columns	10	0	03FEB10 A	22MAR10 A		100
1144	Stonework Under House	3	0	03FEB10 A	05FEB10 A		100
1146	Repair stone retaining wall	2	0	03FEB10 A	22FEB10 A		100
1010	Porch/Foundation Structural Repairs	5	0	08FEB10 A	12FEB10 A		100
1046	Install Steps	10	0	12FEB10 A	18MAR10 A		100
1022	Floor Deck @ Proch	5	0	15FEB10 A	19FEB10 A		100
1034	Sitework	5	0	17FEB10 A	20MAY10 A		100
1016	CMU Block @ Wheelchair Lift	2	0	01MAR10 A	02MAR10 A		100
1036	Stonework @ Ramp	7	0	08MAR10 A	16MAR10 A		100
1028	Install Cistern & Storm Lines	5	0	15MAR10 A	24MAR10 A		100
1026	FloorDeck & HandRail @ Breezeway	5	0	22MAR10 A	06MAY10 A		100
1052	Exterior Paint	20	5	22MAR10 A	08JUN10	21d	75
1012	Breezeway Structural Repair & Decking	10	0	23MAR10 A	06MAY10 A		100
1096	Refurbish Light Fixtures	30	0	23MAR10 A	02JUN10 A		100
1112	Sprinkler Piping @ Breezway	2	0	25MAR10 A	26MAR10 A		100
1124	Refurbish Finish Hardware	25	2	31MAR10 A	03JUN10	11d	92
1260	Install Wheelchair Lift	5	0	06APR10 A	14MAY10 A		100
1080	Electrical rough In Kitchen Building	5	0	07APR10 A	29APR10 A		100
1048	Install Steel Handrails	2	0	19APR10 A	20APR10 A		100
1040	Install Radiant Floor System	15	5	03MAY10 A	08JUN10	7d	67
1062	Plumbing Rough-In	2	0	03MAY10 A	06MAY10 A		100
1082	Interior Carpentry	2	0	03MAY10 A	05MAY10 A		100
1122	STRIP & CLEAN FLOORS	7	2	03MAY10 A	03JUN10	24d	71
1078	Install Light & Plumbing Fixtures	5	5	02JUN10	08JUN10	11d	0
1106	Reinstall Wood Shutters & Screens	3	3	02JUN10	04JUN10	13d	0
1114	Install Chimney Caps	2	2	02JUN10	03JUN10	24d	0
1126	Reinstall Refurbished Finish Hardware	3	3	04JUN10	08JUN10	11d	0
1060	Instulation & Sheathing	10	10	09JUN10	22JUN10	7d	0
1128	Misc Interior Finishes Completion	5	5	14JUN10 *	18JUN10	8d	0
1130	Final Cleanup	5	5	21JUN10	25JUN10	8d	0
1064	Sprinkler Rough-In CrawlSpace	4	4	23JUN10	28JUN10	7d	0
1076	Above Crawlspace Inspection	0	0		23JUN10 *	0	0
1044	Punch Out	10	10	24JUN10	07JUL10	0	0
1132	Crawlspace and Exterior inspection	0	0		30JUN10 *	5d	0

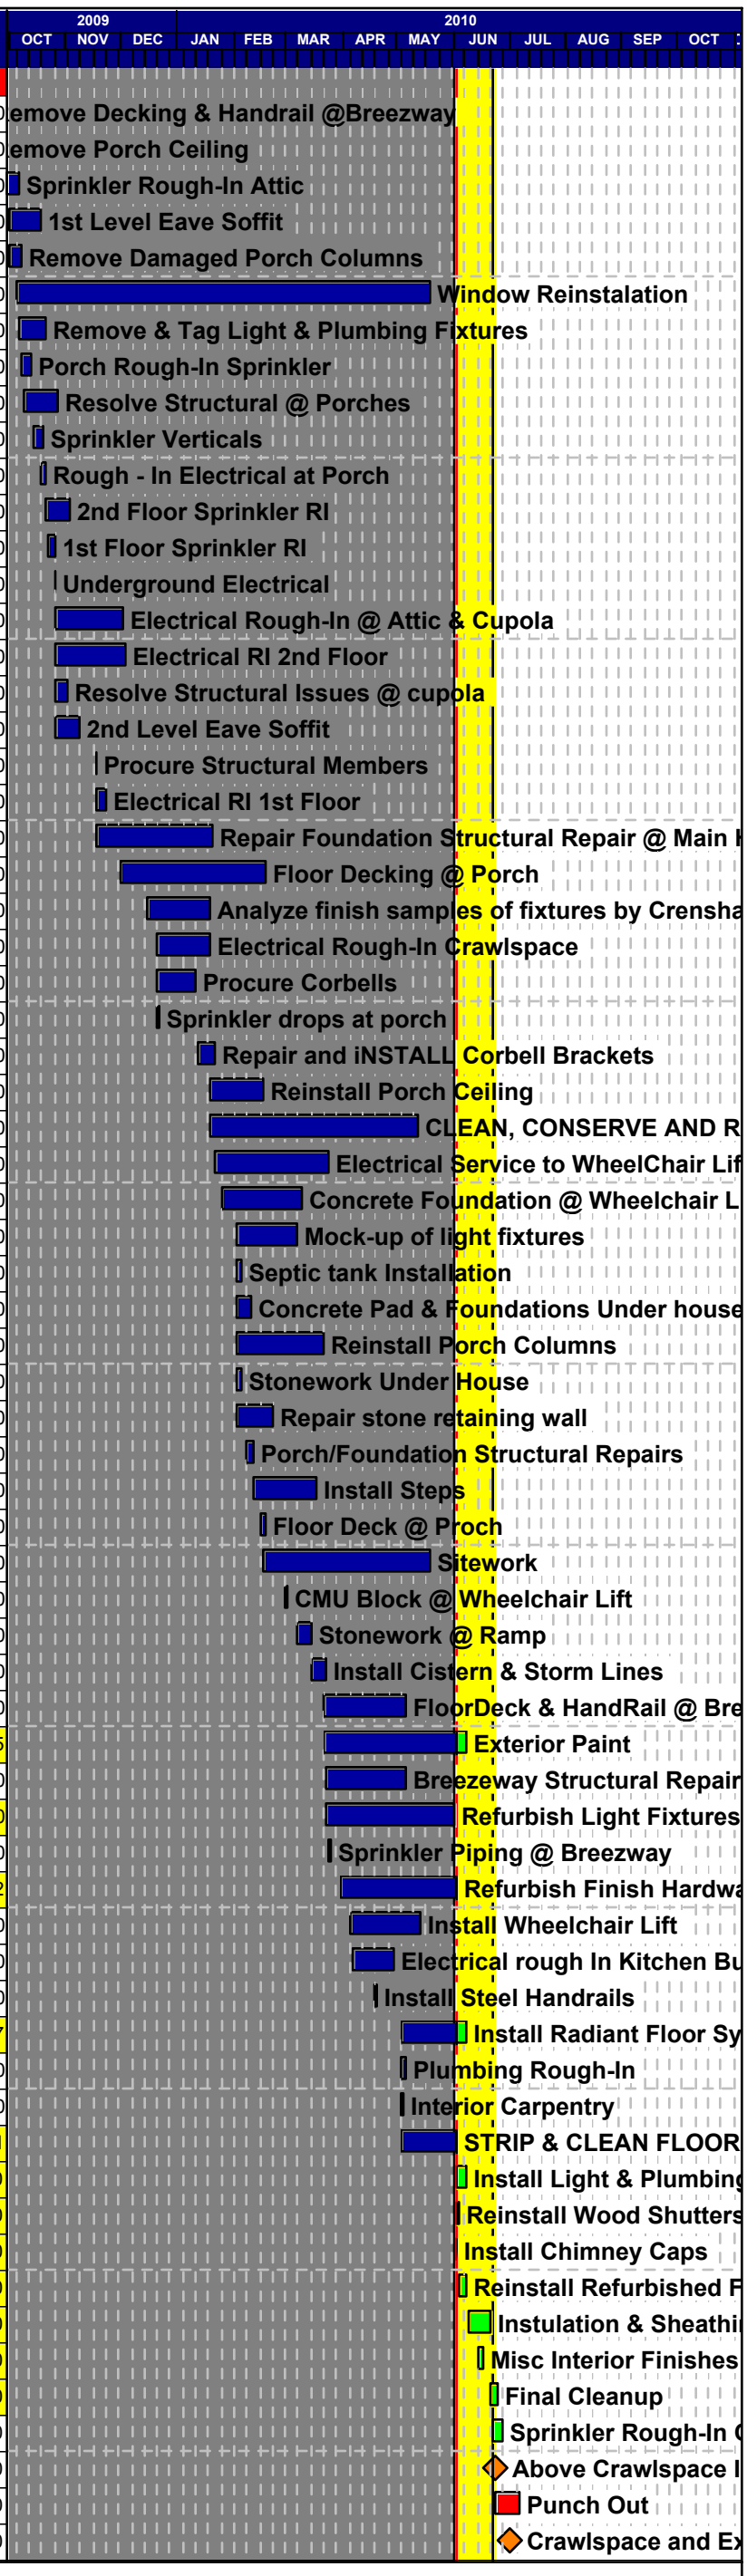

© Primavera Systems, Inc.

Garbutt Construction Company
Hardman Farm Restoration - CCO # 3

Early bar
Progress bar
Critical bar
Summary bar
Start milestone point
Finish milestone poi

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	%
Submittal Scedule							
1200	Resubmit on Sprinkler	5	0	01OCT09 A	14OCT09 A		100
1218	Submit on Wood Shutters & Screens	10	0	05OCT09 A	22JAN10 A		100
1236	Submit on Radiant Heating	15	0	05OCT09 A	29MAR10 A		100
1280	Submit on Interior Millwork	10	0	05OCT09 A	28DEC09 A		100
1268	Submit on Electrical	15	0	07OCT09 A	04NOV09 A		100
1202	Approve Sprinkler Shop Drawings	10	0	14OCT09 A	02NOV09 A		100
1286	Submit on Sitework	10	0	27OCT09 A	18NOV09 A		100
1204	Fabrication and Procurement of Sprinkler	5	0	02NOV09 A	09NOV09 A		100
1242	Submit on Accessories & Specialties	10	0	02NOV09 A	22JAN10 A		100
1262	Submit on Cistern System & Drainage	10	0	04NOV09 A	29JAN10 A		100
1270	Approve Electrical Submittals	10	0	04NOV09 A	19NOV09 A		100
1264	Submit on Sitework	1	0	05NOV09 A	18NOV09 A		100
1254	Submit on Wheelchair Lift	10	0	11NOV09 A	04FEB10 A		100
1232	Approve Insulation	5	0	17NOV09 A	25NOV09 A		100
1230	Submit on Insulation	10	0	18NOV09 A	18NOV09 A		100
1276	Approve Sitework	1	0	18NOV09 A	25NOV09 A		100
1206	Submit on Mortar	10	0	16DEC09 A	13JAN10 A		100
1208	Approval of Masonry Materials	5	0	18DEC09 A	24DEC09 A		100
1272	Procure Electrical Materials	10	0	21DEC09 A	12JAN10 A		100
1234	Procure Insulation	5	0	25DEC09 A	07JAN10 A		100
1282	Approve Interior Millwork	5	0	28DEC09 A	06JAN10 A		100
1212	Submit on Metal Handrails	10	0	06JAN10 A	03FEB10 A		100
1284	Procure Interior Millwork	15	0	06JAN10 A	11MAR10 A		100
1220	Approve Wood Shutters & Screens	10	0	22JAN10 A	27JAN10 A		100
1244	Approval of Accessories & Specialties	5	0	22JAN10 A	27JAN10 A		100
1290	Procure Cistern & Drainage Materials	5	0	25JAN10 A	02MAR10 A		100
1210	Procure Masonry Material	5	0	26JAN10 A	01FEB10 A		100
1246	Procure Accessories& Specialties	10	0	27JAN10 A	05APR10 A		100
1288	Approve Cistern & Site Drainage	10	0	29JAN10 A	16FEB10 A		100
1214	Approve Metal Handrails	5	0	03FEB10 A	05MAR10 A		100
1256	Approve Wheel Chair Lift	5	0	04FEB10 A	08FEB10 A		100
1222	Procure Wood Shutters & Screens	20	0	17FEB10 A	17MAY10 A		100
1266	Procure Cistern System Materials	3	0	17FEB10 A	18FEB10 A		100
1258	Procure Wheelchair Lift	25	0	10MAR10 A	05APR10 A		100
1216	Procur Metal Handrails	10	0	23MAR10 A	19APR10 A		100
1224	Submit on Chimney Caps	10	0	23MAR10 A	26MAR10 A		100
1248	Submit on Plumbing Materials	10	0	23MAR10 A	25MAR10 A		100
1238	Approve Radiant Heating System	2	0	25MAR10 A	10MAY10 A		100
1226	Approve Chimney Caps	2	0	26MAR10 A	26MAR10 A		100
1228	Fab & Procure Chimney Caps	10	0	30MAR10 A	03MAY10 A		100
1240	Procure Radiant Heating Materials	2	0	05APR10 A	12APR10 A		100
1250	Approve Plumbing Materials	2	0	05APR10 A	03MAY10 A		100
1252	Procure Plumbing Materials	2	0	05APR10 A	09APR10 A		100

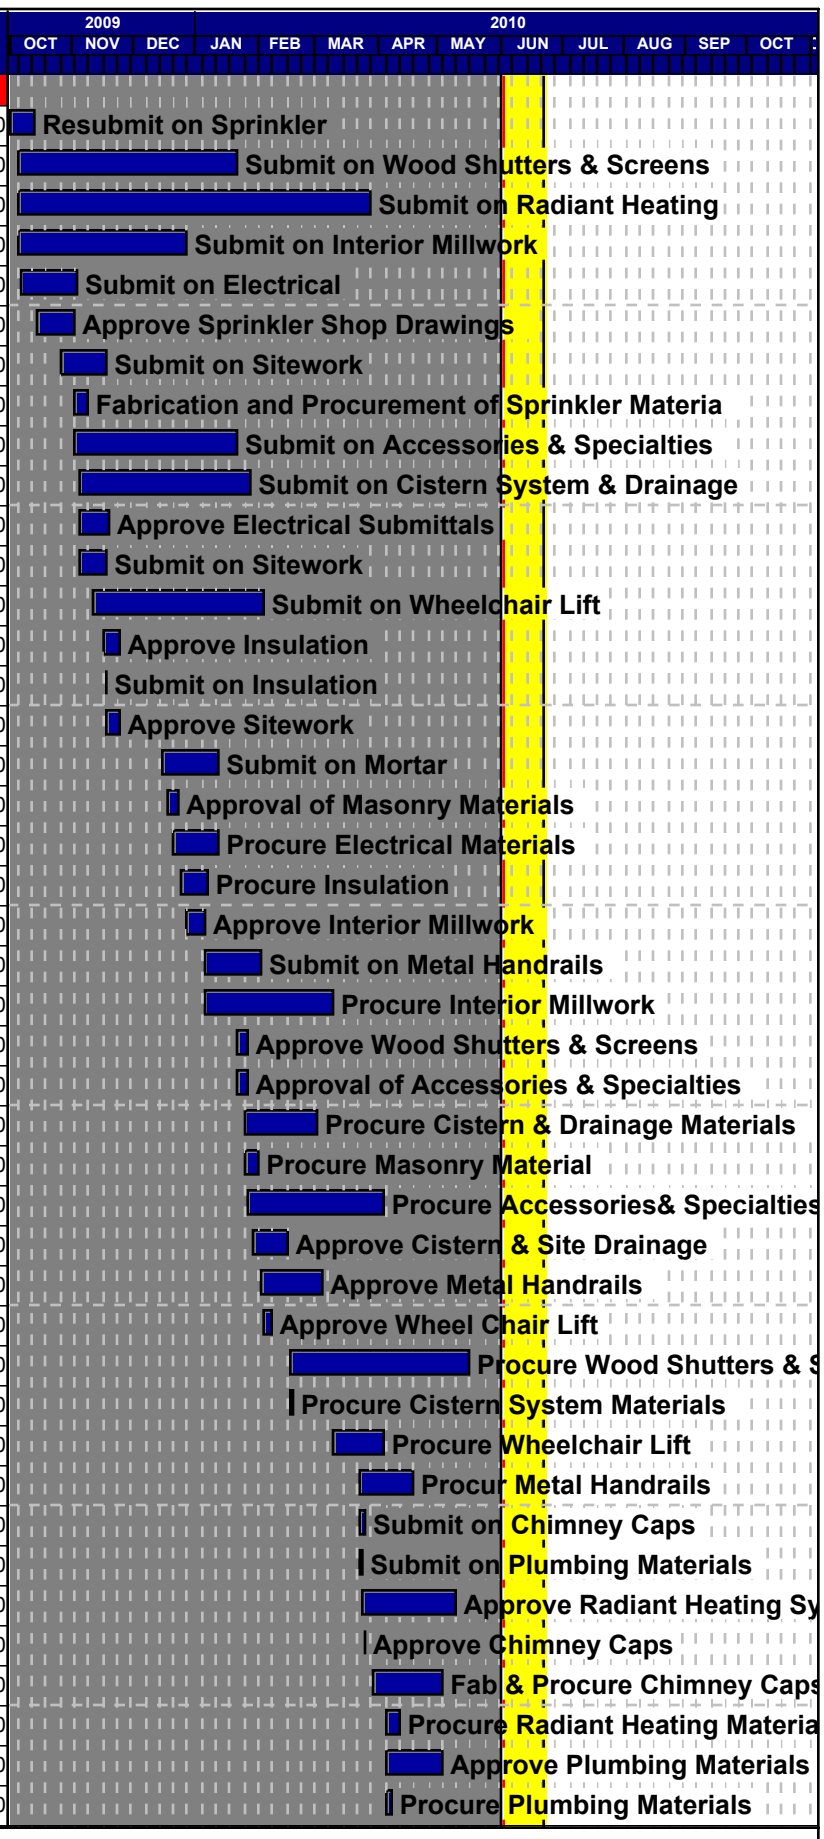

Start date	07OCT09
Finish date	07JUL10
Data date	02JUN10
Run date	02JUN10
Page number	2A

© Primavera Systems, Inc.

Garbutt Construction Company
Hardman Farm Restoration - CCO # 3

Early bar
Progress bar
Critical bar
Summary bar
Start milestone point
Finish milestone point
